



PROJECT: T5686 SR 15/SR600 (SANFORD, 17/92, LAKE MARY) · DATE: JULY 22, 2026 · RECORD ID: 17010CBF

EXECUTIVE SUMMARY · JULY 22, 2026

T5686 SR 15/SR600 (SANFORD, 17/92, LAKE MARY)

20-07 · DR-2026-03522

SAFE DAY

OPERATIONAL SUMMARY · SUPERVISOR ACCEPTED

Field forces installed 120 LF of 18 in storm pipe, set 2 inlets, managed a utility conflict, and maintained trench safety controls while preparing to continue the south run tomorrow.

Approved by certification-script · Accepted 2026-07-22T23:14:29.046749Z

WORK	Directed drainage installation and utility conflict coordination. · Pipe staging, trench cleanup, and grade checks.
PRODUCTION	120.0 LF Storm pipe installed · 2.0 EA Inlets set
CONSTRAINTS	Other (1 RFI · 1 Schedule)
MATERIAL	In: 120 LF 18 in RCP, 18 TON #57 stone
NOTES	Spanish note: Se mantuvo acceso para residentes y se controló el polvo durante toda la jornada.

01 · PROJECT INFORMATION

PROJECT	T5686 SR 15/SR600 (SANFORD, 17/92, LAKE MARY)
PROJECT #	20-07
LOCATION	SANFORD, 17/92, LAKE MARY
DATE	July 22, 2026
REPORT #	DR-2026-03522
PREPARED BY	Cert Foreman
SUPERINTENDENT	Jaymn Judd
WEATHER	Sunny, humid, afternoon storm risk

03 · GENERAL INFORMATION

SCHEDULE DELAYS	No
WEATHER IMPACT	No
ACCIDENTS ON SITE	No
INJURIES REPORTED	No
GENERAL NOTES	Spanish note: Se mantuvo acceso para residentes y se controló el polvo durante toda la jornada.

04 · MASCI CREWS ON SITE

Common schedule · 6:00 AM → 5:00 PM · 11.0 h gross – 0.50 h lunch = 10.50 h net

NAME	EMPLOYEE ID	TRADE / ROLE	START	STOP	LUNCH	HOURS	COST CODE	WORK PERFORMED
Jaymn Judd		Foreman	6:00 AM	5:00 PM	30 min	10.5		Directed drainage installation and utility conflict coordination.
Alejandro Escobedo		General Laborer	6:00 AM	5:00 PM	30 min	10.5		Pipe staging, trench cleanup, and grade checks.
Total Hours						21.00		

05 · SUBCONTRACTORS

COMPANY	TRADE / WORK	HEADCOUNT	HOURS	NOTES
A-1 Block Inc	Materials	1	2	Delivered inlet components.

07 · EQUIPMENT LOG

UNIT / EQUIPMENT	RUN HOURS	IDLE HOURS	TIME DELIVERED	TIME REMOVED	NOTES
305 EX	8		6:15 AM	4:30 PM	Excavator used for trench and pipe placement.
Dump Truck 12	6		7:00 AM	3:45 PM	Spoil haul-off and bedding delivery.

08 · MATERIALS DELIVERED

MATERIAL	QTY	UNIT	CARRIER	TICKET #	COST CODE	NOTES
18 in RCP	120	Linear Feet	A-1 Block Inc	TKT-001		North run install
#57 stone	18	Tons	A-1 Block Inc	TKT-002		Pipe bedding

09A · ACTIVITY PROGRESS

Progress complement to Production Quantities (09b). Station ranges and quantities live in 09b.

ACTIVITY	% DONE	NOTES
Storm pipe installation	65%	Installed 120 LF with laser verification.
Utility conflict coordination	20%	Marked telecom crossing and held excavation.


09B · PRODUCTION QUANTITIES

DESCRIPTION	QTY	UNIT	FROM	TO	NOTES
Storm pipe installed	120.0	Linear Feet	12+00	13+20	18 in RCP
Inlets set	2.0	Each	12+80	13+10	Precast structures
Production Totals	2 Each · 120 Linear Feet				

09C · DELAYS / EXTRA WORK · CONSTRAINTS

TYPE	HOURS	IMPACT	ADVISORY	NOTES
Other	Hours Impacted: 1.5 h		RFI · Schedule	[Delay] Existing utility conflict required hand-dig and locator verification.

10 · PHOTOS

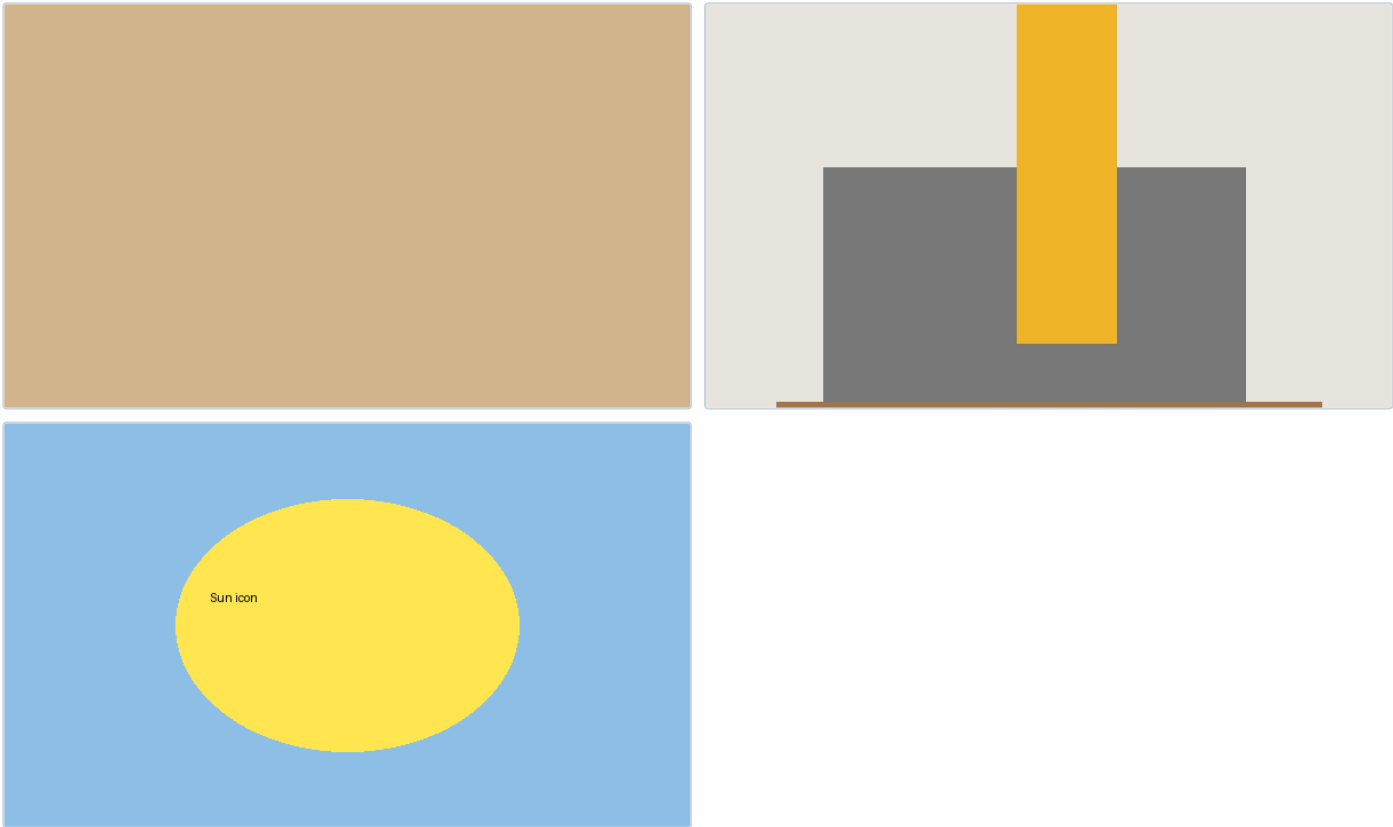

10B · ATTACHMENT & DOCUMENT EVIDENCE

UPLOADED DOCUMENTS

FILENAME	CATEGORY	UPLOADED	ATTACHMENT STATUS
daily_ticket.pdf	PDF	2026-07-22T23:14:28.682827Z	Saved · photo://masci-hub/documents/2026/07/dr_attachmen
notes with spaces & punctuation!.txt	Document	2026-07-22T23:14:29.022927Z	Saved · photo://masci-hub/documents/2026/07/dr_attachmen

These files were attached to the canonical Daily Report record. Extraction results were not persisted on this report, so the PDF is listing the stored evidence references directly.

This platform and training material are provided as a documentation and support tool only and do not replace required safety supervision, inspections, or regulatory compliance responsibilities.

mascidocs.com is a customer-branded deployment of a platform developed by ForgedOps LLC.
